



1. Yes, the estimations were reasonably accurate. The story points were assigned using the Fibonacci scale based on the complexity and effort expected for each task. The larger tasks, such as Detect Downtime and Send Alerts (8 points), required more effort than simpler tasks such as Register a Microservice (3 points).
2. Yes. The backlog was prioritized based on the importance and impact of each requirement. Health monitoring and downtime alerts were given high priority because they are essential for identifying service failures quickly. Less critical features, such as API documentation, were given medium priority.
3. The simulated sprint followed the planned workflow of moving tasks from To Do → In Progress → Done. The highest-priority stories were included in Sprint 1, while the remaining stories were reserved for the next sprint. This helped demonstrate how planned work progresses during a sprint.
4. The burndown chart showed how quickly the team completed the planned story points during the sprint. It helped compare actual progress with the ideal guideline and showed whether the team was completing work at the expected rate. The chart also indicated the team's capacity and helped identify whether work was being completed steadily or concentrated toward the end of the sprint.

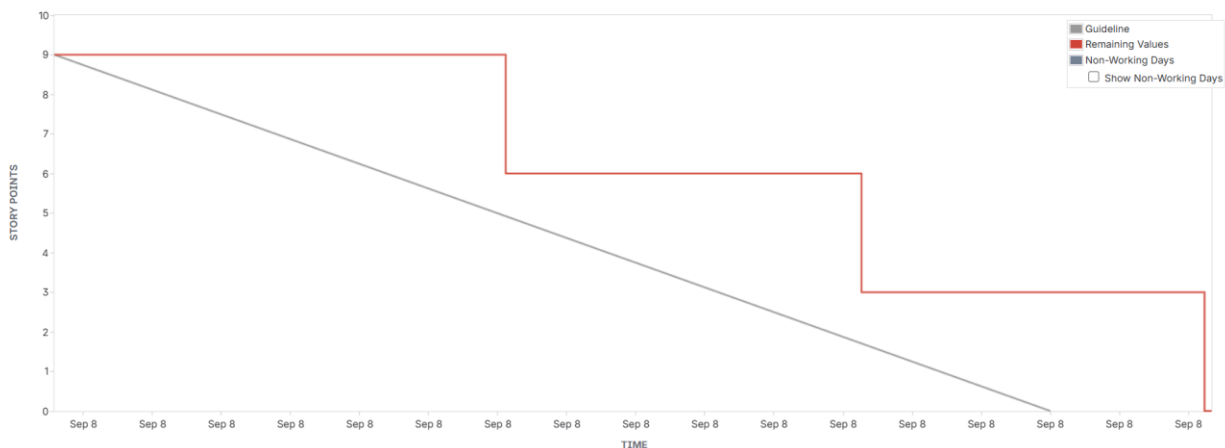

Sprint 2

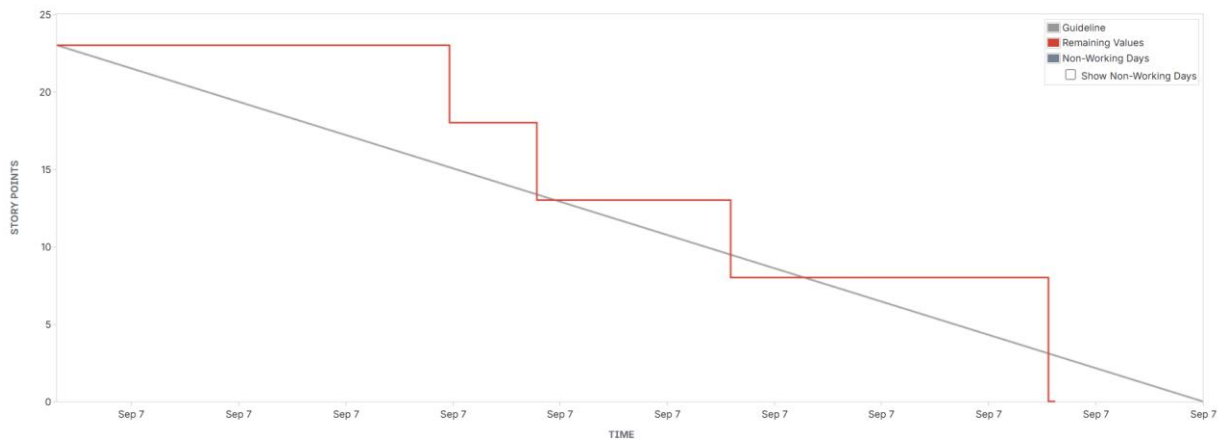

Sprint 1

Epic

No epic

>

Microservice Catalog Management

...

>

Microservice Health Monitoring

...

>

Dependency & API Documentation

...

+ Create epic

Spaces /

Microservices Health...

 /

MHMP-1

Microservice Catalog Management

+

...

▼ Description

Enable DevOps Engineers to register, update, search, and manage microservice information in the internal service catalog.

▼ Attachments

Add attachment

Create project plan

Try

▼ Child work items

...

+

100% Done

Work	Prior...	Story ...	Assi...	Status
✓ MHMP-4 Register a Microservice	^ H...	3	Un:	Done ▼
✓ MHMP-5 Update Microservice Details	= M...	3	Un:	Done ▼

Linked work items

Add linked work item

Microservice Health Monitoring



▼ **Description**

Enable continuous monitoring of registered microservices through automated health probes, availability calculations, downtime detection, and alerts.

▼ **Attachments**



Add attachment

Create project plan [Try](#)

▼ **Child work items**



100% Done

Work	Prior...	Story ...	Assi...	Status
☒ MHMP-6 Monitor Microservice Health	H...	5	Un...	Done
☒ MHMP-7 Calculate 24-Hour Service Availability	H...	5	Un...	Done
☒ MHMP-8 Detect Downtime and Send Alerts	H...	8	Un...	Done

Dependency & API Documentation



▼ **Description**

Provide an interactive view of microservice dependencies and centralized access to API documentation.

▼ **Attachments**



Add attachment

Create project plan [Try](#)

▼ **Child work items**



100% Done

Work	Prior...	Story ...	Assi...	Status
☒ MHMP-9 View Microservice Dependency Graph	H...	5	Un...	Done
☒ MHMP-10 View Aggregated API Documentation	M...	3	Un...	Done

Linked work items

Add linked work item
